

Fix the portfolio's efficiency. Use the festival as the growth engine.

My first month as Music Creator Manager · Belle He · August 2026 · “From your room to the main stage.”

Background. This plan combines a first-month creator portfolio operating plan with an eight-week festival activation roadmap. It draws on conversations with music creators and industry practitioners, and on observations of comparable TikTok LIVE music programs. All assumptions and targets are validated against internal data in week 1.

1 · COACH BY ARCHETYPE

The portfolio's problem is **efficiency, not effort**: the most active creators are declining. I will establish one diagnosis, one priority and one coaching plan for each creator.

→ pages 3-4

2 · FESTIVAL AS GROWTH ENGINE

The **Road to Pulse Creator Program** recruits new music creators, re-energizes existing ones and creates a path from short-form participation to LIVE, monetization and long-term retention.

→ pages 5-7

3 · BASELINE-DISCIPLINED DELIVERY

Targets are set against a defined baseline, **leading indicators gate spending**, and a week-4 checkpoint keeps pacing on plan.

→ pages 2, 8

\$80K

activation budget

8 weeks

to festival, five phases

5 + open

managed creators + open recruitment

ROI ≈ 5-6x

estimated; methodology p.8, recalibrated in week 1

Day 30: five coaching plans live · Road to Pulse launched, entries tracked against the week-4 checkpoint · licensing, stage and partner workstreams on track · a live dashboard running on supply, engagement, creator performance and budget.

A long-term ecosystem framework; the festival is one lever inside it

Scope, baseline and targets come first. Figures below are hypotheses, estimated from industry research and comparable campaigns, to validate in week 1.

1 · VERTICAL DEFINITION & SIZING

- **Pan-music creators:** singing, instruments, DJ sets, production. Broad at the vertical level, precise per creator
- The five managed creators are the showcase anchors; recruitment extends to short-video musicians
- Persona (hypothesis): **16-34, urban, EDM / DJ-culture adjacent**; DJ sets, remixing, singer-songwriters, instrumentalists
- Sizing (hypothesis): a broader pool of tagged music creators exists beyond the current LIVE base; a meaningful portion is active in short-form but not yet on LIVE. Tagging refines this in week 1

2 · BASELINE DISCIPLINE

- Baseline = **7-day averages** at period start and end, outlier days (platform mega-campaigns) removed
- Success is read as **campaign period vs baseline**, never raw totals
- Key campaign actions are scheduled **inside the measurement window**

3 · TARGETS (HYPOTHESES, WITH A BASIS)

- **Vertical:** daily streaming actives +8-10%, daily revenue +12-15% vs baseline; actives carried by tail and new creators, revenue by the top
- **Campaign top creators:** revenue +100%+ during campaign, paying-user share +30-40%, per-payer spend +20-45%, follower growth
- **ROI $\approx$ 5-6x:** methodology and calculation on p.8
- Basis: industry research and comparable-campaign benchmarks, conservative midpoints; recalibrated against internal baseline in week 1

ADDITIONAL INFORMATION I WOULD REQUEST

Internal tier standards and where the five sit · content profiles · ROI & measurement conventions (campaign vs baseline?) · traffic sources, payer concentration, 90-day trends · MoM 0.09/0.22 read as +9%/+22%

PORTFOLIO DIAGNOSIS

The most active creators are declining: an efficiency problem, not an effort problem


Last 30 days. Revenue per LIVE hour spans 5× across the portfolio.

CREATOR	LIVE HRS	AVG CCV	REVENUE	REV / HR	MOM	RETURNING
● Echo Music	38	1,250	\$12,100	\$318	+22%	48%
● Luna Live	58	910	\$17,600	\$303	+9%	60%
● DJ Nova	115	430	\$14,200	\$123	-18%	81%
● BeatTheory	90	310	\$10,400	\$116	-7%	75%
● Vinyl Nights	126	185	\$7,800	\$62	-20%	87%

Hours and growth are **inversely related**: the two creators streaming the most are declining fastest. The portfolio needs **better hours, not more hours**. Portfolio-level: **\$62.1K** total, weighted MoM **-3.4%**; Luna + Echo generate **48% of revenue on 23% of the hours**.

Note: MoM values 0.09 and 0.22 in the source table are read as +9% and +22%.

RETURNING VIEWERS VS. REVENUE GROWTH (MOM)

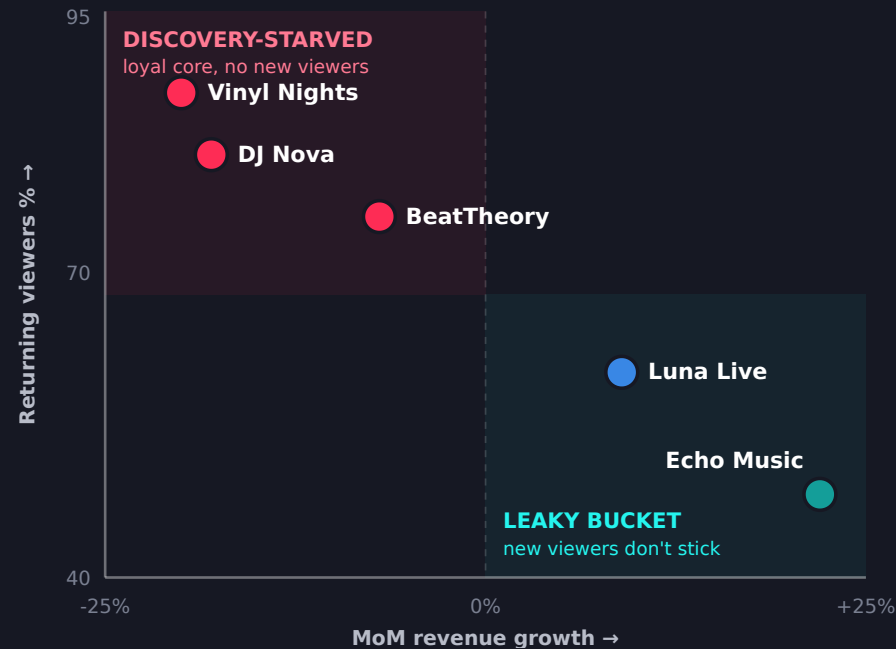

Verdicts — BACK: Echo (P1), Luna · FIX: Nova, Vinyl · HOLD: BeatTheory. Three patterns: leaky-bucket risers, discovery-starved loyalists, balanced. Operating actions: p.4.

One plan per creator: back the winners, fix the leaks

Coaching effort goes where it changes the trajectory; every plan is validated in week-1 1:1s.

Echo Music · BACK · P1 — momentum is perishable: fixed schedule; 1v1 dedicated management; welcome rituals and fresh hooks for new-viewer conversion; fan-community VIP events (themed parties, birthdays, creator-planned) to consolidate paying users

DJ Nova · FIX — refreshed show formats and new segments; off-peak tests; festival stage slot as a new-audience injection

BeatTheory · HOLD — prevention: run Luna's playbook, one new-format experiment per month, alert on early echo-chamber signals

Luna Live · BACK — codify her playbook portfolio-wide; gentle hours increase. Balance can also mean a ceiling: content review before scaling

Vinyl Nights · FIX — fewer, better hours (126 → ~80); new show formats; co-streams with rising creators; creator×fan second-creation missions

Execution notes — moves fit stable-but-stalling creators; avoid homogenized content; keep a 10% backup roster, outreach never converts 100%

HOW TO MEASURE · COACHING SUCCESS (PER CREATOR)

Streaming actives & hours · watch UV · follower growth · revenue · paying-user share · per-payer spend · watch → pay conversion. Targets are set in week-1 1:1s against each creator's own baseline, referencing comparable-campaign benchmarks.

One festival, three funnels: recruit the new, energize the existing, showcase the top

The plan: “**From Your Room to the Main Stage**” · the Road to Pulse Creator Program, in five phases.

Of the many possible plays, this program concentrates on **two mechanisms not yet tried in this vertical but proven elsewhere**: a creator×fan second-creation loop, and event marketing that amplifies showcases.

1 · Sign-up & warm-up · W1-2

2 · Launch · W2

3 · Online rounds · W3-6

4 · Festival weekend · W7-8

5 · Post-festival push · W8+

detail: p.8

RECRUIT

The **Rising division** of Road to Pulse: a dedicated on-ramp for musicians who have never gone LIVE. Short-video missions count as entry, so the funnel starts one level below the official campaigns’ eligibility gates.

Feeds: daily streaming actives, new-creator supply

ENERGIZE

Existing creators compete in the **Headliner division**; a 4-week bootcamp covers streaming craft and the monetization ladder; portfolio creators mentor and perform, which doubles as their discovery fix.

Feeds: engagement, revenue, portfolio recovery

SHOWCASE


The **TikTok LIVE stage at Pulse**: competition finals and top-talent performances, all streamed to the platform. The stream is the product for the 99% who are not on site.

Feeds: platform heat, brand, showcase goal

Budget sits in the appendix (p.8), concentrated on stage + competition: they compound, and marketing amplifies what they create.

Road to Pulse: On Deck’s proven architecture, with a wider entry gate

Deliberately copied where proven; my changes target recruiting pre-LIVE musicians and day-31 aftercare.



THE REWARD LADDER (CAREER CAPITAL OVER CASH)

All entrants	Pulse avatar frame + campaign badge	≈ \$0, platform asset
Round winners	Diamonds + festival merch	low
Semifinalists	VIP Pulse tickets, travel covered	the bulk of \$18K
Top 3	Stage slot + distribution support + own track as a limited-run LIVE Gift	≈ \$0, platform access

The top of the ladder is platform access, not cash. Mirrors On Deck: Breakaway, Music On Stage and Songs of LIVE mechanics.

INSIDE EVERY ENTRANT’S ROOM

- Campaign-exclusive **Pulse Gift** with in-room counter; milestone progress bar unlocks reward tiers
- **Live rank badge**; leaderboard resets weekly
- **Shout-out segment**: entrants thank top supporters on air, a built-in retention ritual

Creatorxfan second creation & spread. Fan clip missions ranked by like tiers, offered 1v1 to high-stickiness, mass-fan creators; open clip rights; attendee UGC via booth QR. Topic planning and pre-planned collaborative moments run through a partner amplification network; top creators post through the campaign (≥80% participation target). These mechanics are new to this vertical (proven in comparable ecosystems); sizing and payout impact will be measured against internal data after onboarding.

On site, the festival is a stage and a content factory

Three days of festival, eight weeks of content, and partner relationships that outlive the event.

ON-SITE DELIVERY

- **Sponsorship** covers non-content site costs; stage & show programming curated from competition winners
- **Discovery booth**: attendees start their first LIVE with staff guidance
- **QR attribution**: stage and booth codes deep-link to each creator’s LIVE, so impact is measurable per creator
- **On-site clipping desk**: same-day highlight clips feed the hashtag while the festival is still on

PARTNER MANAGEMENT

- **Festival org**: deliverables SLA + weekly sync; stage specs, VIP-ticket inventory and booth placement locked by W6
- **Program team**: measured on qualified creators + platform heat; we deliver pre-event posting in return
- **BD team** assists recruitment; **product team** ships custom event effects; **labels** clear licensing from W1

CORE PLAN VS STRETCH PLAN · SEPARATED BY RESOURCE ASSUMPTIONS

Core (committed)	Runs on confirmed resources only: competition + finale on a licensed catalog cleared in W1; stage and booth per the signed SLA; ≥90% sessions delivered; zero material rights or safety incidents
Stretch (if resources land)	Star anthem collaboration and artist co-streams (artist & label approval); custom event effects (product bandwidth); a breakout showcase push toward a 5,000+ concurrent-viewer moment

HOW TO MEASURE · DELIVERY PLAN, GOVERNANCE & RISK

Four workstreams, seven decision points, one weekly rhythm

WORKSTREAM	W1-2	W3-4	W5-6	W7-8
Competition & campaign	Sign-up opens; mechanics tested; live end of W2	Weekly rounds; W4 entries checkpoint	Rounds close W5; semifinal W6; finalists locked	Rehearsal W7; “The Final Drop” W8
Creator coaching	1:1 diagnoses validated; plans live	Archetype moves running	Mid-point review; adjust	Stage prep; festival performances
Marketing & second creation	Anthem seeding; topic planning	Fan-clip missions; weekly highlights	Semifinal push; ≥80% creator posting	Finale spike; on-site UGC
On-site & partners	Kickoff; licensing starts; SLA signed	Offline build from W3	Specs, VIP inventory, booth frozen W6	Delivery + wrap

Decision points: W2 launch · W4 entries checkpoint · W5 qualifiers · W6 finalists · W7 lock · W8 delivery · W+4 retention report | PM dimensions covered: time (weeks), scope (phases & funnels), quality (gates & guardrails), cost (budget below)

TOP RISKS → MITIGATIONS

Music licensing gaps	Rights + replacement tracks from W1; no uncleared set on stage
Recruitment shortfall	Agency pre-commitments; 20–30% over-provision + 10% backup; W4 boost
On-site tech / brand safety	Redundant streams + W7 rehearsal; moderation coverage, T&S escalation pre-agreed
Gift-vote gaming	Judge-score gate + anomaly monitoring
Budget overrun	8% contingency + weekly burn review

HOW TO MEASURE · PROJECT METRICS

Leading · supply	500+ entries; 150+ first LIVEs; quality-weighted hours; bootcamp ≥60%
Process · engagement	Vertical watch UV/time; new-viewer share ↑ (Nova & Vinyl); ACV ↑
Lagging · revenue	Portfolio MoM positive by W8; payer share +30–40%; per-payer +20–45%; D30 ≥40%
Auxiliary · showcase heat	1–2 creators break 5,000 concurrent viewers (incumbents + finalists); post-campaign review: did a vertical benchmark emerge
Guardrails · execution	≥90% sessions delivered; zero material incidents; within \$80K

Supply and retention are the cause; revenue is the effect. Targets estimated from industry research and comparable campaigns; recalibrated in week 1.

ROI methodology. ROI = incremental campaign-window revenue ÷ \$80K. Estimate: portfolio uplift ≈\$70K + participating-creator uplift ≈\$250K + new-creator revenue ≈\$80K → ≈\$400K, ROI ≈5×. Aligned to the internal incremental-ROI convention in week 1. **Budget:** stage & production \$28K · prizes & travel \$18K · marketing \$16K · bootcamp \$8K · on-site ops \$4K · contingency \$6K.

Recommendation: approve this plan, subject to week-1 validation of baseline data, the rights inventory and partner deliverables. I look forward to discussing these assumptions and mechanisms further in the interview.
