

Fix the portfolio's efficiency. Use the festival as the growth engine.

My first month as Music Creator Manager · Belle He · August 2026 · “From your room to the main stage.”

Background. This plan combines a first-month creator portfolio operating plan with an eight-week festival activation roadmap. It draws on conversations with music creators and industry practitioners, and on observations of comparable TikTok LIVE music programs. All assumptions and targets are validated against internal data in week 1.

1 · COACH BY ARCHETYPE

The portfolio's problem is **efficiency, not effort**: the most active creators are declining. I will establish one diagnosis, one priority and one coaching plan for each creator.

→ pages 3-4

2 · FESTIVAL AS GROWTH ENGINE

The **Road to Pulse Creator Program** recruits new music creators, re-energizes existing ones and creates a path from short-form participation to LIVE, monetization and long-term retention.

→ pages 5-7

3 · BASELINE-DISCIPLINED DELIVERY

Targets are set against a defined baseline, **leading indicators gate spending**, and a week-4 checkpoint keeps pacing on plan.

→ pages 2, 8

\$80K

activation budget

8 weeks

to festival, five phases

5 + open

managed creators + open recruitment

ROI ≈ 5-6x

estimated; methodology p.2, recalibrated in week 1

DAY 30 · WHAT IS ALREADY LIVE

- Five coaching plans live, one per creator
- Licensing, stage and partner workstreams on track
- Road to Pulse launched; entries tracked against the week-4 checkpoint
- Live dashboard on supply, engagement, creator performance and budget

A long-term ecosystem framework; the festival is one lever inside it

Scope, baseline and targets come first; figures are hypotheses from industry research and comparable campaigns, validated in week 1.

1 · VERTICAL DEFINITION & SIZING

- **Pan-music creators:** singing, instruments, DJ sets, production. Broad at the vertical level, precise per creator
- The five managed creators are the showcase anchors; recruitment extends to short-video musicians
- Persona (hypothesis): **16-34, urban, EDM / DJ-culture adjacent**; DJ sets, remixing, singer-songwriters, instrumentalists
- Sizing (hypothesis): a broader pool of tagged music creators sits beyond the current LIVE base, many active in short-form but not yet LIVE; tagging refines this in week 1

2 · BASELINE DISCIPLINE

- Baseline = **7-day averages** at period start and end, outlier days (platform mega-campaigns) removed
- Success is read as **campaign period vs baseline**, never raw totals
- Key campaign actions are scheduled **inside the measurement window**

3 · TARGETS (HYPOTHESES, WITH A BASIS)

- **Vertical:** daily streaming actives +8-10%, daily revenue +12-15% vs baseline; actives carried by tail and new creators, revenue by the top
- **Campaign top creators:** revenue +100%+ during campaign, paying-user share +30-40%, per-payer spend +20-45%, follower growth
- **ROI $\approx 5-6\times$** = incremental campaign-window revenue $\div$ \$80K. Estimate: portfolio uplift $\approx$ \$70K + participating-creator uplift $\approx$ \$250K + new-creator revenue $\approx$ \$80K $\rightarrow \approx$ \$400K, ROI $\approx 5\times$; aligned to the internal incremental-ROI convention in week 1
- Basis: comparable-campaign benchmarks at conservative midpoints; recalibrated against internal baseline in week 1

ADDITIONAL INFORMATION I WOULD REQUEST

- Internal tier standards and where the five sit
- ROI & measurement conventions (campaign vs baseline?)
- Confirm MoM 0.09/0.22 reads as +9%/+22%
- Content profiles of the five creators
- Traffic sources, payer concentration, 90-day trends

PORTFOLIO DIAGNOSIS


The most active creators are declining: an efficiency problem, not an effort problem

Last 30 days. Revenue per LIVE hour spans 5× across the portfolio.

CREATOR	LIVE HRS	AVG CCV	REVENUE	REV / HR	MOM	RETURNING
Echo Music	38	1,250	\$12,100	\$318	+22%	48%
Luna Live	58	910	\$17,600	\$303	+9%	60%
DJ Nova	115	430	\$14,200	\$123	-18%	81%
BeatTheory	90	310	\$10,400	\$116	-7%	75%
Vinyl Nights	126	185	\$7,800	\$62	-20%	87%

Hours and growth are **inversely related**: the two creators streaming the most are declining fastest. The portfolio needs **better hours, not more hours**. Portfolio-level: **\$62.1K** total, weighted MoM **-3.4%**; Luna + Echo generate **48% of revenue on 23% of the hours**.

RETURNING VIEWERS VS. REVENUE GROWTH (MOM)

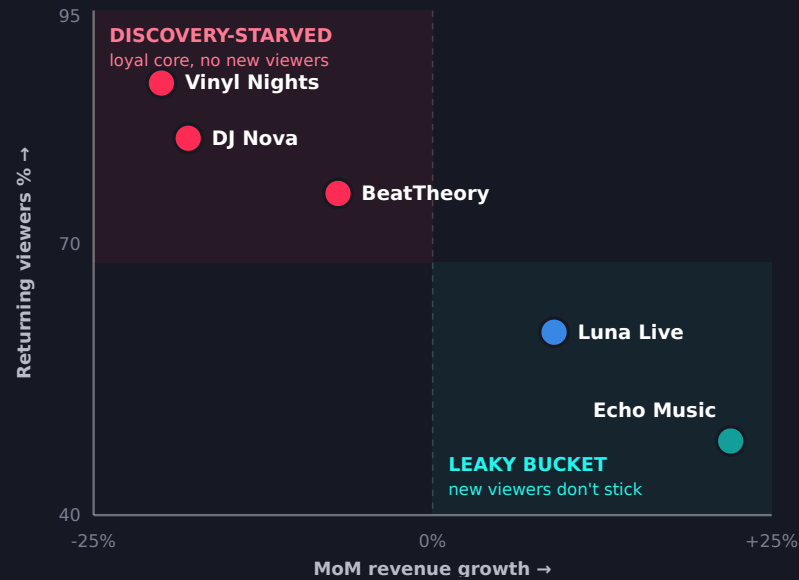

DATA CONCLUSIONS · OPERATING ACTIONS: P.4

BACK · Echo (P1) & Luna

Top revenue per hour (\$318 / \$303); the only positive MoM (+22% / +9%); Luna balanced on every column

HOLD · BeatTheory

Same pattern at an early stage (-7%, returning 75%); prevention, not rescue

FIX · Nova & Vinyl

Most hours streamed (115 / 126) yet steepest decline (-18% / -20%); returning 81% / 87% with almost no new viewers

Patterns & offset

Leaky-bucket risers / discovery-starved loyalists / balanced; sample may drift in execution — keep a 10% backup roster

Strategy by tier: back the winners, fix the leaks, hold the middle

One action per line; every plan is validated in week-1 1:1s.

TIER 1 · BACK · ECHO (P1), LUNA

- Fixed schedule + 1v1 dedicated management (Echo)
- Fan-community VIP events: themed parties, birthdays, creator-planned, to consolidate paying users
- Welcome rituals + fresh hooks for new-viewer conversion
- Codify Luna's playbook portfolio-wide; gentle hours increase (balance can mean a ceiling: content review first)

TIER 2 · FIX · NOVA, VINYL

- Refresh show formats and add new segments
- Off-peak tests (Nova); fewer, better hours 126 → ~80 (Vinyl)
- Co-streams with rising creators; festival stage slots as a new-audience injection
- Creator×fan second-creation missions

HOLD · BEATTHEORY + EXECUTION NOTES

- Run Luna's playbook; one new-format experiment per month
- Alert on early echo-chamber signals
- Moves fit stable-but-stalling creators; avoid homogenized content
- Keep a 10% backup roster; outreach never converts 100%

HOW TO MEASURE · COACHING SUCCESS, PER CREATOR, IN TWO DIMENSIONS

ACTIVITY

- Daily streaming actives
- Streaming hours
- Watch UV
- Follower growth +xx

REVENUE

- Daily revenue
- Paying-user share +xx
- Per-payer spend +xx
- Watch → pay conversion

Targets are set in week-1 1:1s against each creator's own baseline, referencing comparable-campaign benchmarks. Coaching results are read separately from campaign effects: a creator can improve before the festival ever starts.

One festival, three funnels: recruit the new, energize the existing, showcase the top

The plan: “**From Your Room to the Main Stage**” · the Road to Pulse Creator Program, in five phases.

Of the many possible plays, this program concentrates on **two mechanisms not yet tried in this vertical but proven elsewhere**: a creator×fan second-creation loop, and event marketing that amplifies showcases.




BUDGET (\$80K) · CONCENTRATED ON STAGE + COMPETITION — THEY COMPOUND



- Pacing: ≈40% warm-up / 40% campaign & festival / 20% tail
- Creator-directed spend: ≈50% to top + high-potential, the rest to recruitment

Road to Pulse: On Deck’s proven architecture, with a wider entry gate

Deliberately copied where proven; my changes target recruiting pre-LIVE musicians and day-31 aftercare.



THE REWARD LADDER (CAREER CAPITAL OVER CASH)

All entrants	Pulse avatar frame + campaign badge	≈ \$0, platform asset
Round winners	Diamonds + festival merch	low
Semifinalists	VIP Pulse tickets, travel covered	the bulk of \$18K
Top 3	Stage slot + distribution support + own track as a limited-run LIVE Gift	≈ \$0, platform access

The top of the ladder is platform access, not cash. Mirrors On Deck: Breakaway, Music On Stage and Songs of LIVE mechanics.

INSIDE EVERY ENTRANT’S ROOM

- Campaign-exclusive **Pulse Gift** with in-room counter; milestone progress bar unlocks reward tiers
- **Live rank badge**; leaderboard resets weekly
- **Shout-out segment**: entrants thank top supporters on air, a built-in retention ritual

CREATOR×FAN SECOND CREATION

- Fan clip missions ranked by like tiers; **open clip rights** so fans can cut freely
- Offered **1v1** to high-stickiness, mass-fan creators; payer structure decides who runs fan campaigns
- Attendee UGC collected on site via booth QR

AMPLIFICATION & SPREAD

- Topic planning and **pre-planned collaborative moments** run through a partner amplification network
- Top creators post through the campaign; **≥80% participation target**

These mechanics are new to this vertical (proven in comparable ecosystems); sizing and payout impact will be measured against internal data after onboarding.

On site, the festival is a stage and a content factory

Three days of festival, eight weeks of content, and partner relationships that outlive the event.

ON-SITE DELIVERY

- **Sponsorship** covers non-content site costs; stage & show programming curated from competition winners
- **Discovery booth**: attendees start their first LIVE with staff guidance
- **QR attribution**: stage and booth codes deep-link to each creator’s LIVE, so impact is measurable per creator
- **On-site clipping desk**: same-day highlight clips feed the hashtag while the festival is still on

PARTNER MANAGEMENT

- **Festival org**: deliverables SLA + weekly sync; stage specs, VIP-ticket inventory and booth placement locked by W6
- **Program team**: measured on qualified creators + platform heat; we deliver pre-event posting in return
- **BD team** assists recruitment; **product team** ships custom event effects; **labels** clear licensing from W1

CORE PLAN VS STRETCH PLAN · SEPARATED BY RESOURCE ASSUMPTIONS

Core (committed)	Runs on confirmed resources only: competition + finale on a licensed catalog cleared in W1; stage and booth per the signed SLA; ≥90% sessions delivered; zero material rights or safety incidents
Stretch (if resources land)	Star anthem collaboration and artist co-streams (artist & label approval); custom event effects (product bandwidth); a breakout showcase push toward a 5,000+ concurrent-viewer moment

TOP RISKS → MITIGATIONS

Music licensing gaps	Rights + replacement tracks from W1; no uncleared set on stage
Recruitment shortfall	Agency pre-commitments; 20–30% over-provision + 10% backup; W4 boost
On-site tech / brand safety	Redundant streams + W7 rehearsal; moderation coverage, T&S escalation pre-agreed
Gift-vote gaming	Judge-score gate + anomaly monitoring
Budget overrun	8% contingency + weekly burn review

HOW TO MEASURE · DELIVERY PLAN & GOVERNANCE

Five workstreams, seven decision points, one weekly rhythm

Delivery risks and mitigations: p.7. Budget: p.5. ROI methodology: p.2.

WORKSTREAM	DRI	KEY COLLABORATORS	W1-2	W3-4	W5-6	W7-8
Creator portfolio coaching	Music Creator Manager	Data Science; Creator Networks	Validate diagnoses; set baselines; 1:1 plans live	Format, schedule and retention tests; W4 reallocation decision	Review results; lock festival roles	Capture festival conversion; post-event plans
Recruitment, competition & education	MCM / Program Ops	Product; Marketing; Creator Networks	Rising + Headliner entry opens; partner outreach; bootcamp prep	Weekly rounds; bootcamp live; W4 entry checkpoint	Semifinals; finalists locked by W6	Final at Pulse; incubation begins
Marketing & creator amplification	Marketing	Creators; Pulse; sponsor brands	Big idea; creator toolkit; warm-up content	Competition highlights; fan clips; partner distribution	Creator collaborations; finalist stories; countdown	Festival push; recap; retention tail
Sponsorship & commercial partnerships	BD / Partnerships	MCM; Pulse; Legal; Finance	Inventory, target list, rate card, outreach	Shortlist; proposal alignment; W4 commercial checkpoint	Agreements, rights, assets and placements locked by W6	Activation delivery; sponsor reporting
On-site, rights, safety & measurement	Event Ops	Pulse; Legal & Licensing; Product; Data Science; Trust & Safety	Kickoff; SLA; rights inventory; attribution plan	Stage and booth build; vendor plan; product scope confirmed	Rights, logistics, stage specs and safety plan locked	W7 full rehearsal; W8 delivery; QR attribution live

Decision points: W2 launch · W4 go/no-go · W5 qualifiers · W6 finalists & locks · W7 rehearsal lock · W8 delivery · W+4 retention report

PM dimensions: time (weeks) · scope (workstreams) · quality (gates & guardrails) · cost (budget p.5; ROI p.2)

HOW TO MEASURE · PROJECT METRICS

Leading · supply	500+ entries; 150+ first LIVES; quality-weighted hours; bootcamp ≥60%
Process · engagement	Vertical watch UV/time; new-viewer share ↑ (Nova & Vinyl); ACV ↑
Lagging · revenue	Portfolio MoM positive by W8; payer share +30-40%; per-payer +20-45%; D30 ≥40%
Auxiliary · showcase heat	1-2 creators break 5,000 concurrent viewers (incumbents + finalists); post-campaign review: did a vertical benchmark emerge
Guardrails · execution	≥90% sessions delivered; zero material incidents; within \$80K

Supply and retention are the cause; revenue is the effect. Targets estimated from industry research and comparable campaigns; recalibrated in week 1. ROI methodology: p.2.

Recommendation: approve this plan, subject to week-1 validation of baseline data, the rights inventory and partner deliverables. I look forward to discussing these assumptions and mechanisms further in the interview.
